



June 17, 2022

DOWNTOWN ALMONTE CONSTRUCTION 2022-2023

Construction Update

Cavanagh Construction is currently working within Phase A of the downtown core reconstruction project. Efforts are focused on the installation of new watermain and sanitary sewer systems. This work is scheduled to continue over the next month.

Watermain / Sanitary Sewer


Watermain and sanitary sewer installation is in progress along Mill Street.

Storm

In preparation for next week's storm sewer work, Cavanagh has hired a subcontractor to core a hole through the existing concrete and stone wall located between the bridge and the parking lot to 7 Mill Street. This work allows for the installation of pipe through the wall for water to discharge into the Mississippi River.

Traffic

A full road closure has been in effect since May 2nd, 2022, beginning at Almonte Street, and progressing up Mill Street towards Brae Street. Accessibility to businesses that require deliveries and or access will be accommodated. As construction progresses, access from Almonte Street will be restored. The yellow highlighted section in the rendering below indicates the area currently under construction within Phase A.

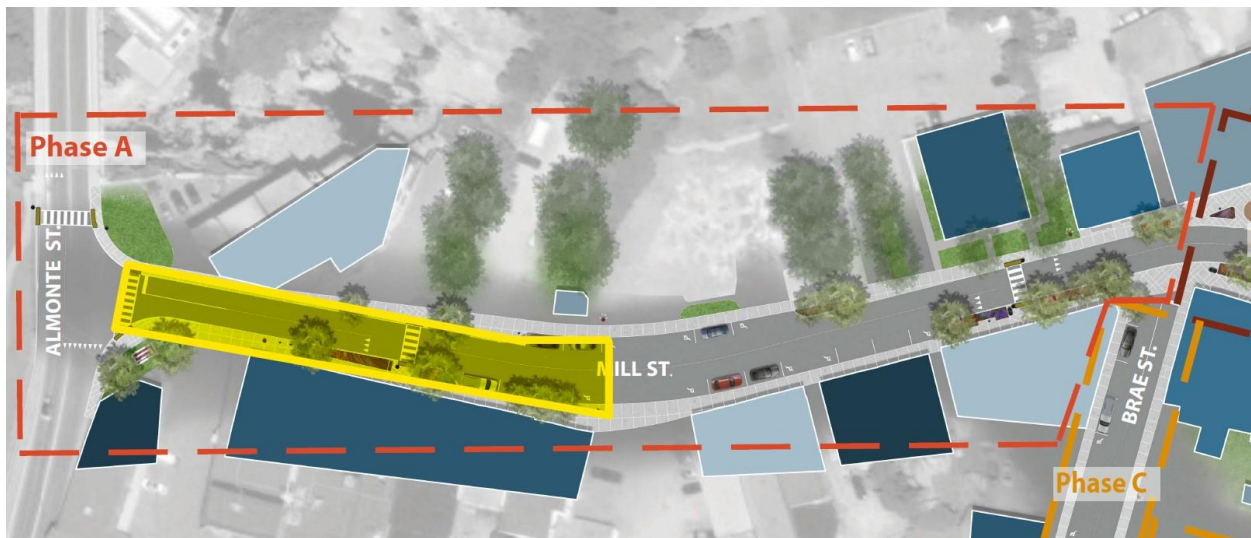

Cavanagh Construction Contact Info

Cavanagh Construction has delivered their notification to residents and businesses; they can be contacted at the following:

Hilary Lalonde

Project Manager
Thomas Cavanagh Construction Ltd.
Cell: 613-298-8524
Email: HLalonde@thomascavanagh.ca

ALTERNATE AFTER HOURS

Nathan Drew

Sewer & Water Superintendent
Thomas Cavanagh Construction Ltd.
Cell: 613-314-5782

Randy Kubusheskie

Roads Superintendent
Thomas Cavanagh Construction Ltd.
Cell: 613-913-9252

For More Information

We request that property owners and businesses provide contact information to ensure you receive any future notifications. Emails can be sent directly to the project manager listed below. Should you have **any** questions, comments or concerns related to the project or require special accessibility accommodations, please let us know by contacting the project manager noted below. Your communication is critical to ensure this project is a successful one.

The Municipality of Mississippi Mills would like to thank you for your patience and co-operation during this construction project.

Robert Smith

Project Manager
Roads & Public Works Technologist
Mississippi Mills
613 256 2064 x233
smithr@mississippimills.ca

Cory Smith

A/ Director of Roads & Public Works
Mississippi Mills
613 256 2064 x229
csmith@mississippimills.ca
